



ADCO/ALTEN JV
Glenview Elementary School, (Schedule subject to Change)
9-3-19

Activity ID	Description	Early Start	Early Finish	RD	Dur	2019											
						AUG		SEP			OCT			NOV			
						26	02	09	16	23	30	07	14	21	28	04	11
Building Exterior																	
West																	
52110	Bldg Paper for Plaster	01JUL19 A	29AUG19 A	0	10	Bldg Paper for Plaste											
52130	Mesh for Plaster	08JUL19 A	29AUG19 A	0	10	Mesh for Plaste											
52140	Scratch Coat	26AUG19 A	06SEP19	4	4	Scratch Coat											
52180	Brown Coat Cure	26AUG19 A	11SEP19	7	10	Brown Coat Cur											
52190	Brown Coat	26AUG19 A	06SEP19	4	4	Brown Coa											
52150	Plaster Finsh	09SEP19	13SEP19	5	5	Plaster Finst											
52400	Down Spouts	16SEP19	27SEP19	10	10	Down Spout											
52700	Exterior Painting West	16SEP19	27SEP19	10	10	Exterior Painting Wes											
East																	
53600	Cont. 2 Horz Z-Girts	08AUG19 A	12SEP19	8	14	Cont. 2 Horz Z-Girts											
53700	3 type 3 Insulation	08AUG19 A	11SEP19	5	5	3 type 3 Insulatic											
53800	Install Windows	12AUG19 A	06SEP19	4	20	Install Window											
53620	Cure Window Caulking	13AUG19 A	09SEP19	5	1	Cure Window Caulkin											
53900	Cont. 1 Vert Z-Girts	14AUG19 A	12SEP19	8	14	Cont. 1 Vert Z-Girts											
53920	Building Paper for Plaster	04SEP19	18SEP19	11	10	Building Paper for Plaste											
45940	Install Storefront	06SEP19 A	19SEP19	5	10	Install Storefron											
53810	Window Testing ??????????	10SEP19	07OCT19	20	20	Window Testing ?????????'											
53940	Mesh for Plaster	12SEP19	25SEP19	10	10	Mesh for Plaste											
53210	Glazing	20SEP19	26SEP19	5	5	Glazing											
53870	Brown Coat	23SEP19	27SEP19	5	5	Brown Coa											
53880	Brown Coat cure	23SEP19	04OCT19	10	10	Brown Coat cur											
53960	Scratch Coat	23SEP19	27SEP19	5	5	Scratch Coat											
Building Roof																	
Built up Roofing East																	
64190	MEP Hook Ups at HVAC	05AUG19 A	16SEP19	10	10	MEP Hook Ups at HVAC Equipme											
Built up Roofing West																	
62920	Install roof ladders	28FEB19 A	17SEP19	2	2	Install roof ladder											
63020	MEP Hook Ups at HVAC	05AUG19 A	16SEP19	10	10	MEP Hook Ups at HVAC Equipme											
Standing Seam Metal Roofing																	

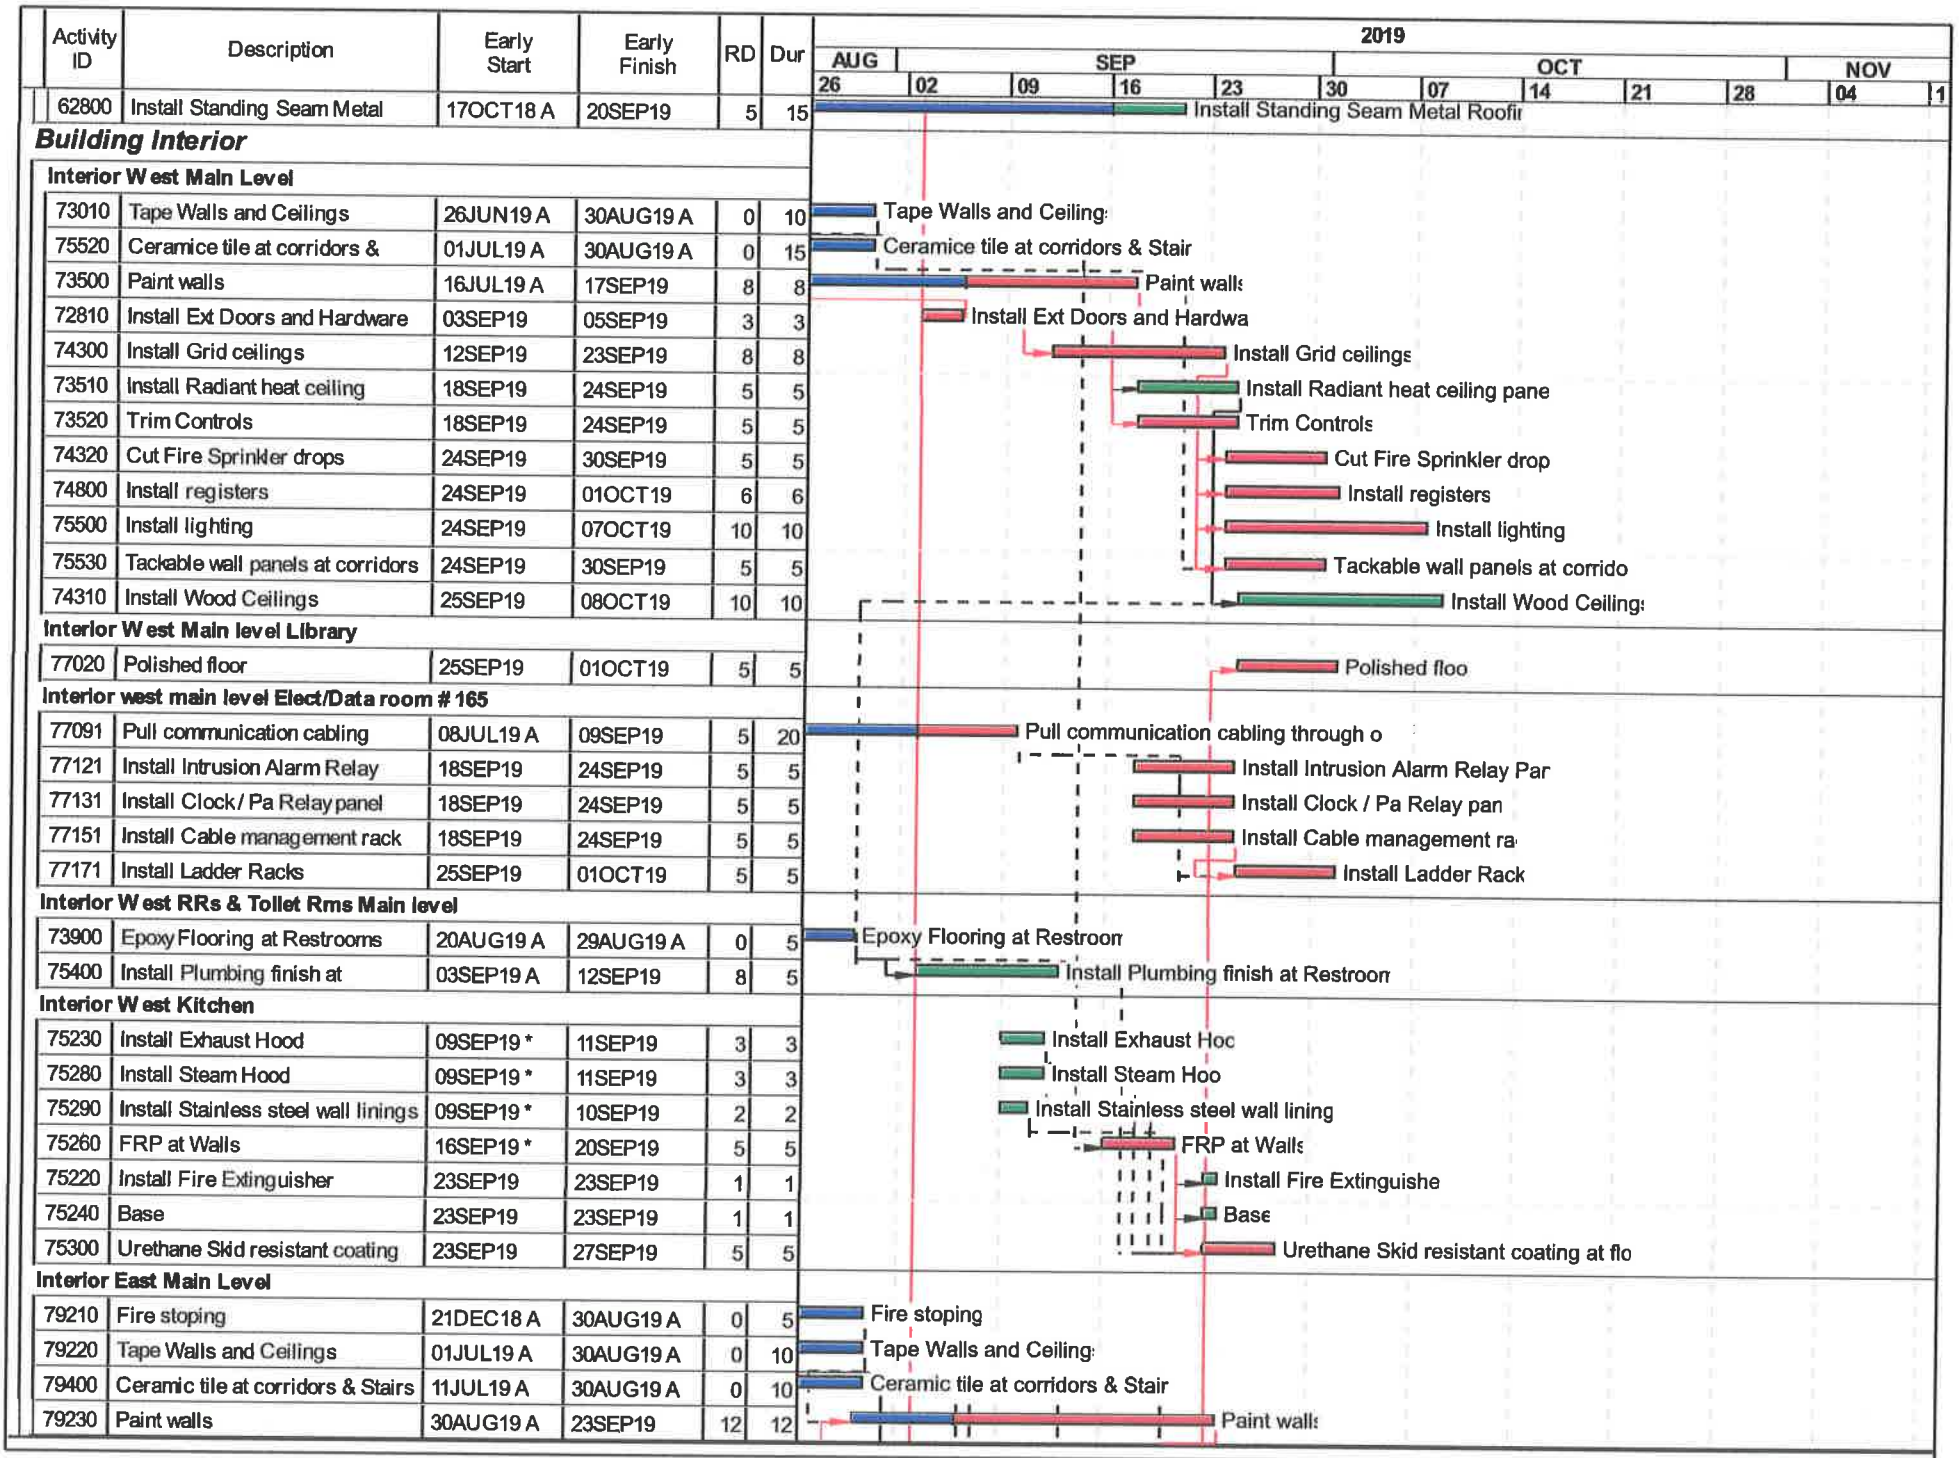

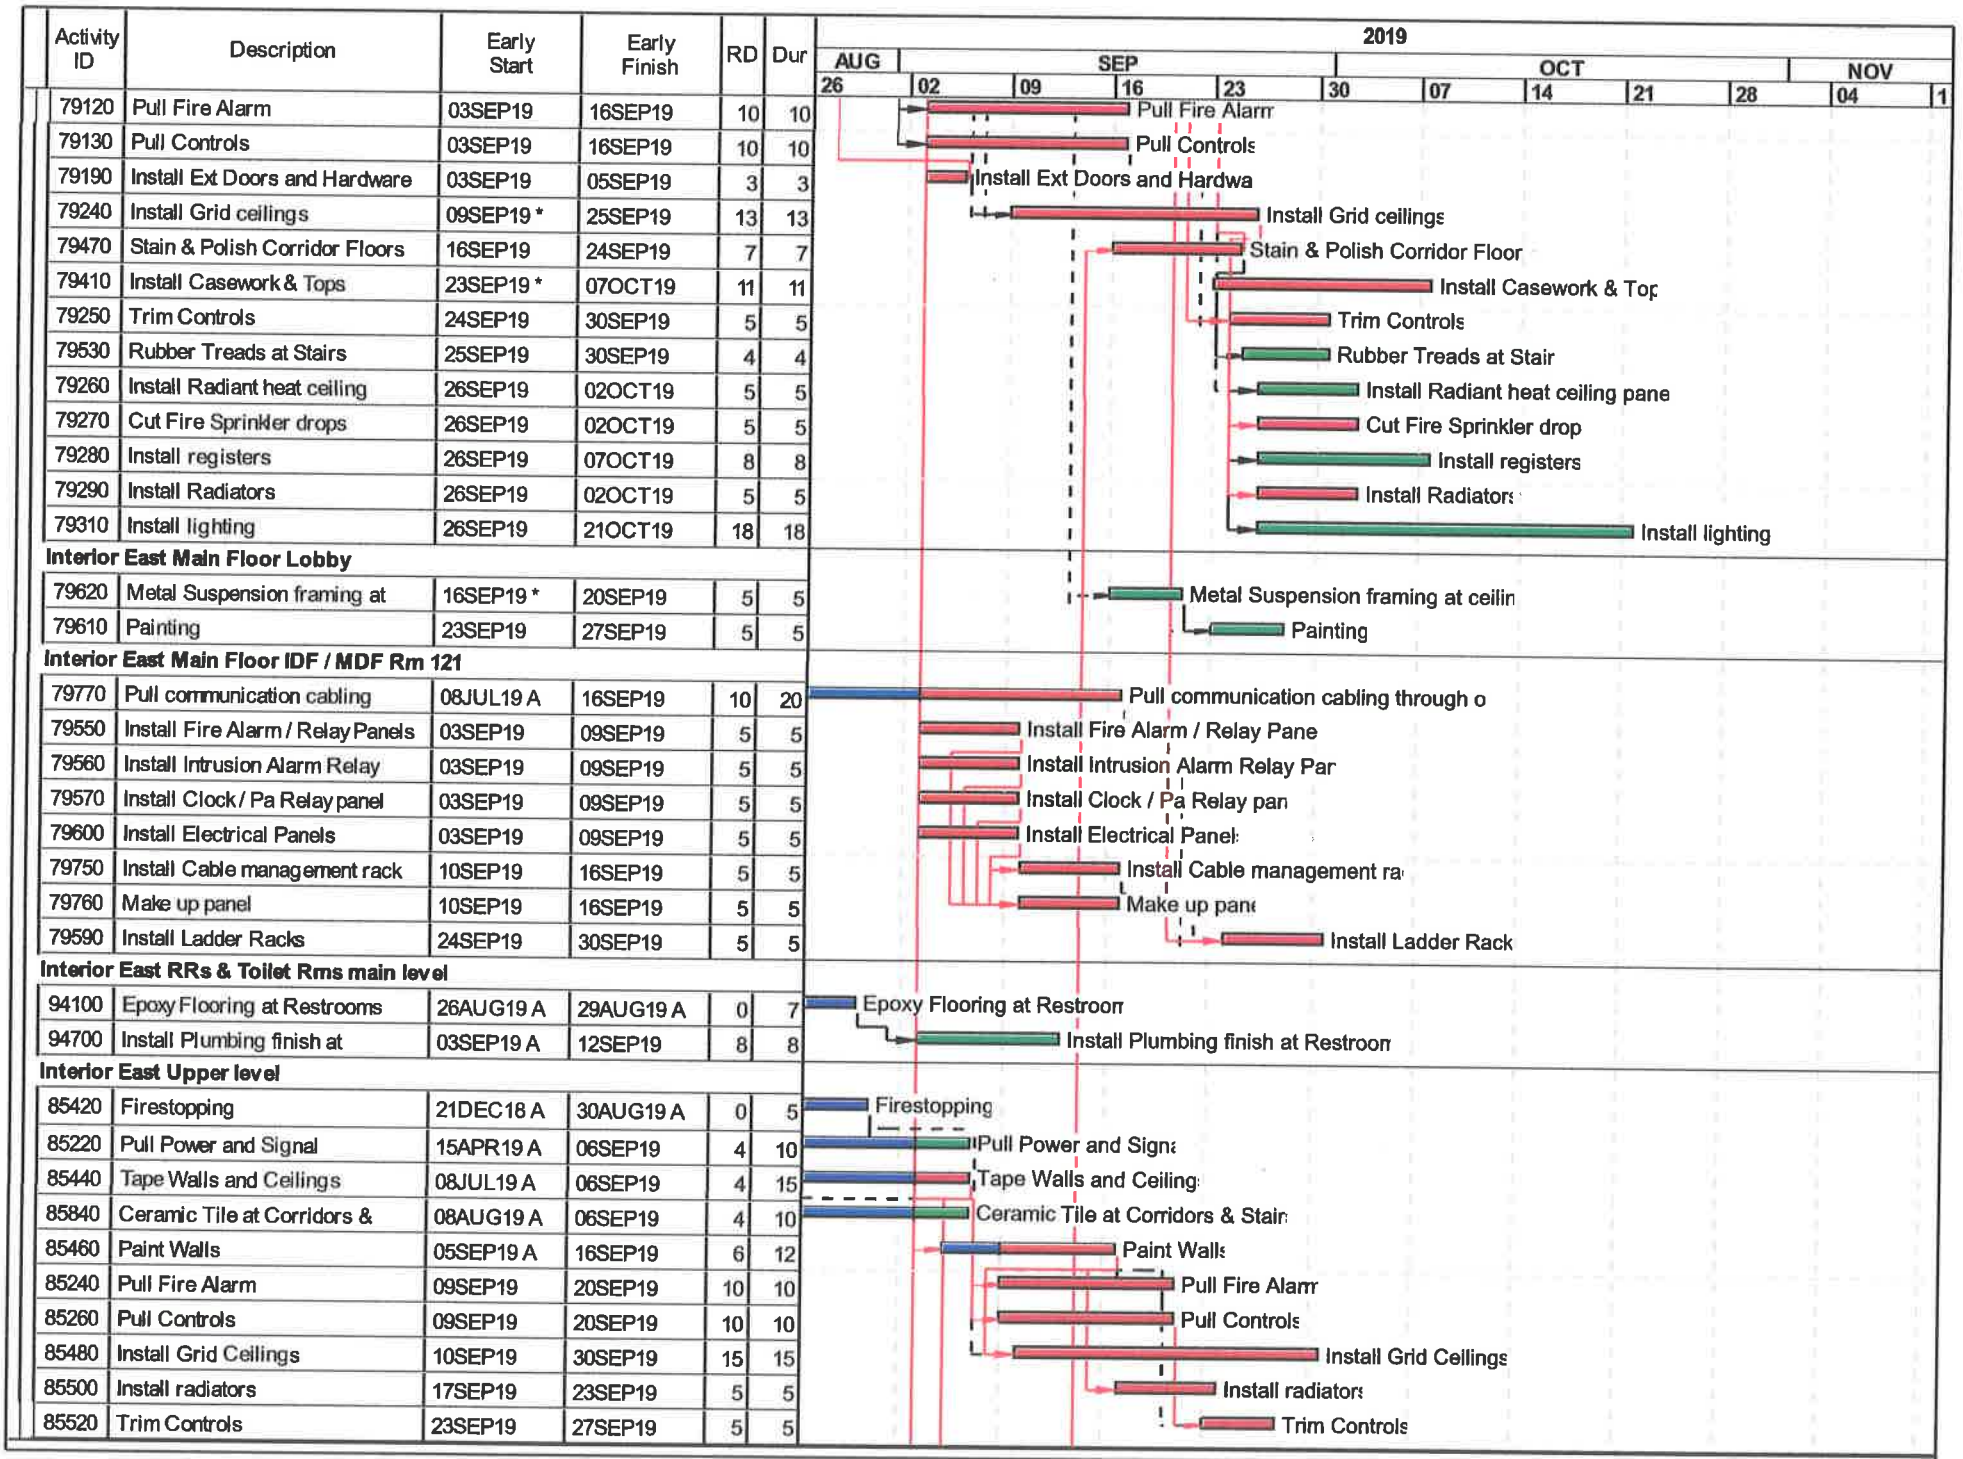

Activity ID	Description	Early Start	Early Finish	RD	Dur	2019											
						AUG		SEP				OCT				NOV	
						26	02	09	16	23	30	07	14	21	28	04	11
82710	Mount BMS Panel	03SEP19 *	04SEP19	2	2	Mount BMS Panel											
82735	Insulate and Label Piping	23SEP19	27SEP19	5	5	Insulate and Label Piping											
82737	Rough in Controls	23SEP19	27SEP19	5	5	Rough in Controls											
Interior Basement Elevator and Machine Room																	
77205	Install Guildrails	09SEP19	12SEP19	4	4	Install Guildrails											
Interior West Gymnasium																	
77180	Pull Power and signal	26MAR19 A	12SEP19	8	8	Pull Power and signal											
77280	Gyp Walls	26JUN19 A	06SEP19	4	5	Gyp Walls											
77140	R.I. Duct work	30AUG19 A	24SEP19	16	16	R.I. Duct work											
77320	Fire stoping	30AUG19 A	05SEP19 A	0	5	Fire stoping											
77340	Tape Walls	09SEP19	23SEP19	11	11	Tape Walls											
77200	Pull Fire Alarm	24SEP19	03OCT19	8	8	Pull Fire Alarm											
77220	Pull Controls	24SEP19	03OCT19	8	8	Pull Controls											
77360	Paint walls	24SEP19	03OCT19	8	8	Paint walls											
New Site (Increment #3)																	
Site Utilities & AC Paving																	
25350	Trench/bed/pipe & backfill Fire	07NOV18 A	17SEP19	5	5	Trench/bed/pipe & backfill Fire Water On S											
25480	PX permit Pending ?	26AUG19 A	05SEP19	3	4	PX permit Pending											
25520	PX Permit Precon	09SEP19 *	09SEP19	1	1	PX Permit Precon											
25490	Remob for site Utilities??	10SEP19 *	10SEP19	1	1	Remob for site Utilities??											
23140	Trench/bed/pipe & backfill PG&E	11SEP19	17SEP19	5	5	Trench/bed/pipe & backfill PG&E Elect Off S											
25370	Trench/bed/pipe & backfill PG&E	11SEP19 *	24SEP19	10	10	Trench/bed/pipe & backfill PG&E Elect On S											
25390	Trench/bed/pipe & backfill	11SEP19 *	24SEP19	10	10	Trench/bed/pipe & backfill AT&T& Comcast On S											
25465	Trench/bed/pipe & backfill PG&E	11SEP19 *	25SEP19	11	11	Trench/bed/pipe & backfill PG&E Gas prim											
25460	Trench/bed/pipe & backfill Fire	18SEP19 *	01OCT19	10	10	Trench/bed/pipe & backfill Fire Alar											
25360	Trench/bed/pipe& backfill AT&T&	25SEP19 *	01OCT19	5	5	Trench/bed/pipe& backfill AT&T& Comcast Off S											
25440	Form & Pour Transformer pad	25SEP19	01OCT19	5	5	Form & Pour Transformer pad											
25470	Form & Pour Gas Meter pad	26SEP19	02OCT19	5	5	Form & Pour Gas Meter pad											
Site Hardscape																	
East Courtyard site work																	
29090	Backfill at walls	08AUG19 A	13SEP19	9	1	Backfill at wall:											
29440	Drainage behind walls	08AUG19 A	13SEP19	9	5	Drainage behind wall											
29080	Underground water for Drinking	16SEP19 *	19SEP19	4	4	Underground water for Drinking founte											
29380	Irrigation mains	16SEP19 *	19SEP19	4	4	Irrigation mains											
29500	Stair Rebar	16SEP19 *	19SEP19	4	4	Stair Rebar											
29560	Form Stairs	20SEP19	26SEP19	5	5	Form Stairs											
29640	Pour stairs	27SEP19	01OCT19	3	3	Pour stairs											
