


ADCO/TUNER/ALTEN JV
Glenview Elementary School, (Schedule subject to Change)
2-4-19

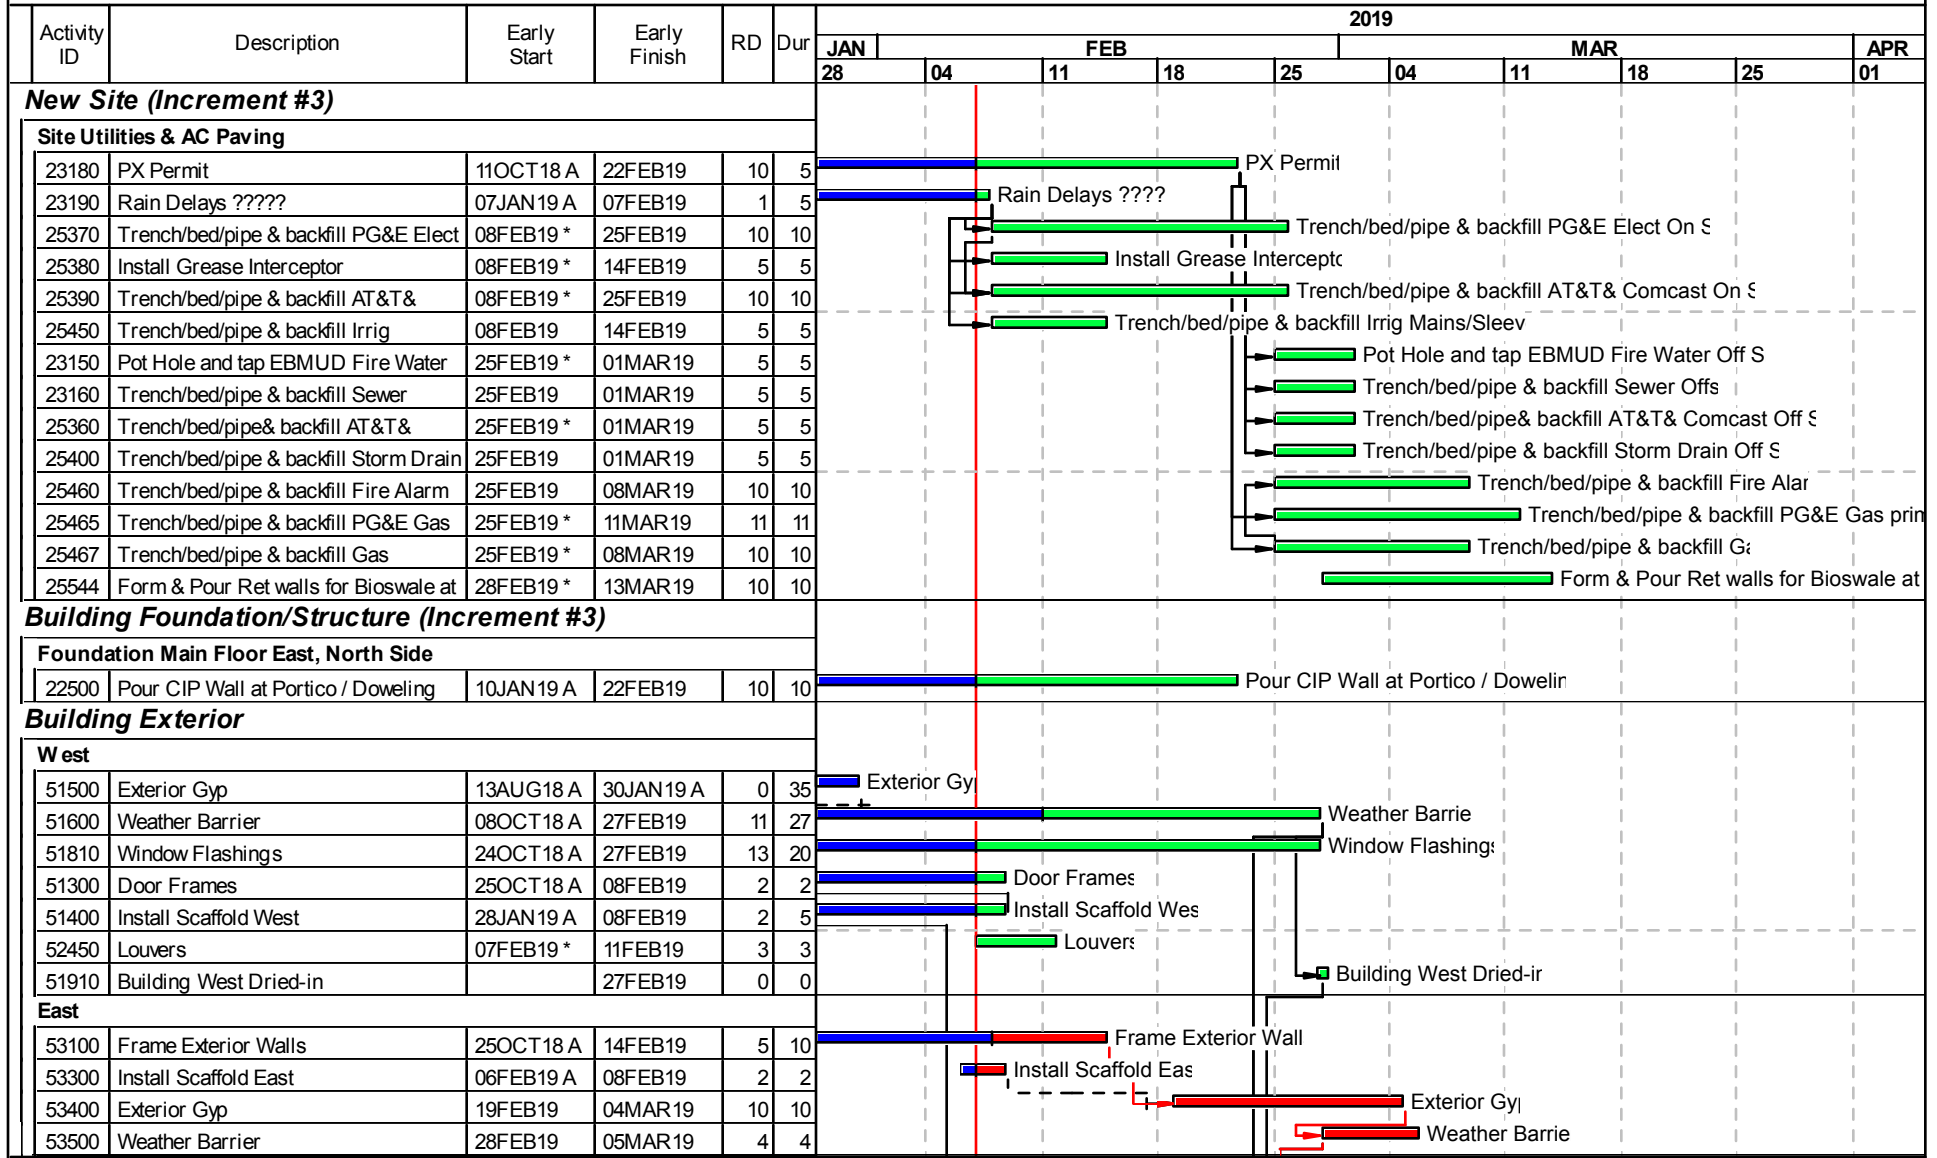

Activity ID	Description	Early Start	Early Finish	RD	Dur	2019											
						JAN		FEB				MAR				APR	
						28	04	11	18	25	04	11	18	25	01		
Building Roof																	
Built up Roofing East																	
64100	Built-up Roofing East, include canopy	28DEC18 A	01FEB19 A	0	4	Built-up Roofing East, include canopy											
Standing Seam Metal Roofing																	
62800	Install Standing Seam Metal Roofing	17OCT18 A	25FEB19	10	15	Install Standing Seam Metal Roofing											
Building Interior																	
Interior East Main Level																	
79100	R.I. Duct work	01OCT18 A	25FEB19	10	20	R.I. Duct work											
79140	Install Fire smoke Dampers	26FEB19	04MAR19	5	5	Install Fire smoke Damper											
79150	Insulate walls	28FEB19 *	06MAR19	5	5	Insulate wall:											
Interior East Upper level																	
85080	R.I. Power and Signal	01OCT18 A	11FEB19	2	30	R.I. Power and Signal											
85100	R.I. Fire Alarm	01OCT18 A	11FEB19	2	30	R.I. Fire Alarm											
85110	R.I. Controls	01OCT18 A	08FEB19	2	15	R.I. Controls											
85320	Install Door Frames	24JAN19 A	13FEB19	5	7	Install Door Frame											
85280	Install Fire Smoke Dampers	07FEB19	13FEB19	5	5	Install Fire Smoke Damper											
85300	Insulate Walls	28FEB19	06MAR19	5	5	Insulate Wall:											
Interior Basement Electrical Room																	
81930	Install SWBD (HMDP)	23AUG18 A	13FEB19	5	10	Install SWBD (HMDP)											
81920	Install panel cans	11OCT18 A	01FEB19 A	0	10	Install panel can											
81940	Install transformer	11OCT18 A	01FEB19 A	0	10	Install transforme											
81950	Install Dist Panel	11OCT18 A	01FEB19 A	0	10	Install Dist Pane											
81960	Install INV Cabinets	11OCT18 A	22FEB19	10	10	Install INV Cabinet											
81990	R.I. Conduit between power equipment	11OCT18 A	01MAR19	5	5	R.I. Conduit between power equipme											
82110	Install Clock/ Relay Panel	11OCT18 A	13FEB19	5	5	Install Clock/ Relay Pan											
82120	Install Intrusion Alarm Panel	11OCT18 A	13FEB19	5	5	Install Intrusion Alarm Pan											
82130	Install Fire Alarm Panels	11OCT18 A	13FEB19	5	5	Install Fire Alarm Panel											
Interior Basement Mechanical Room																	
82050	Rough in Electrical to Equipment	08FEB19	12FEB19	3	3	Rough in Electrical to Equipmer											
82710	Mount BMS Panel	08FEB19	11FEB19	2	2	Mount BMS Pane											
82720	Rough in Gas Piping to Equipment	08FEB19	14FEB19	5	5	Rough in Gas Piping to Equipmer											
82737	Rough in Controls	13FEB19	21FEB19	5	5	Rough in Controls											
82735	Insulate and Label Piping	25FEB19	01MAR19	5	5	Insulate and Label Pipir											
Interior West Main Level																	
71500	R.I. Duct work	26OCT18 A	25FEB19	10	16	R.I. Duct work											
72200	Pull Power and signal	21JAN19 A	21FEB19	8	8	Pull Power and signa											
72300	Pull Fire Alarm	21JAN19 A	21FEB19	8	8	Pull Fire Alarm											
72400	Pull Controls	21JAN19 A	21FEB19	8	8	Pull Controls											
72000	Install Fire smoke Dampers	26FEB19	04MAR19	5	5	Install Fire smoke Damper											
72500	Insulate walls	28FEB19	06MAR19	5	5	Insulate wall:											
Interior West Gymnasium																	

Activity ID	Description	Early Start	Early Finish	RD	Dur	2019											
						JAN			FEB			MAR			APR		
						28	04	11	18	25	04	11	18	25	01		
77080	R.I. Power and signal	13SEP18 A	11FEB19	2	22	R.I. Power and signal											
77120	R.I. Controls	13SEP18 A	14FEB19	5	24	R.I. Controls											
77260	Install door frames	09JAN19 A	08FEB19	2	2	Install door frame											
77140	R.I. Duct work	26FEB19	19MAR19	16	16	R.I. Duct work											
77240	Insulate walls	28FEB19	06MAR19	5	5	Insulate wall											
Site Hardscape																	
East Courtyard site work																	
29440	Drainage behind walls	26NOV18 A	14FEB19	5	5	Drainage behind wall											
29460	Backfill ramp/ret walls	26NOV18 A	14FEB19	5	5	Backfill ramp/ret wall											
29450	Rain Delay	04DEC18 A	07FEB19	1	5	Rain Delay											
29080	Underground water for Drinking	19FEB19	22FEB19	4	4	Underground water for Drinking founta											
29380	Irrigation mains	19FEB19	22FEB19	4	4	Irrigation mains											
29500	Stair Rebar	19FEB19	22FEB19	4	4	Stair Rebar											
29560	Form Stairs	25FEB19	01MAR19	5	5	Form Stairs											
East Perimeter walls along street sidewalk																	
27320	Dig Ftgs for Conc Wall Along Street	27AUG18 A	25FEB19	5	5	Dig Ftgs for Conc Wall Along Street Sidewa											
27340	Rebar Ftgs for Conc wall along street	30AUG18 A	22FEB19	4	4	Rebar Ftgs for Conc wall along street sidewa											
27360	Rebar Temp Ftgs Conc wall along	30AUG18 A	26FEB19	3	3	Rebar Temp Ftgs Conc wall along street sidewa											
27380	Vert Rebar for Conc wall along street	31AUG18 A	27FEB19	2	2	Vert Rebar for Conc wall along street sidewa											
27420	Pour Ftgs for Conc wall along street	13SEP18 A	27FEB19	4	6	Pour Ftgs for Conc wall along street sidewa											
27440	Form One side	21FEB19	27FEB19	5	5	Form One side											
27460	Wall rebar	26FEB19	28FEB19	3	3	Wall rebar											
27480	Double up forms	27FEB19	05MAR19	5	5	Double up form											
West Courtyard / Playard site work																	
23170	Scaffold up at the west	07FEB19	26FEB19	12	12	Scaffold up at the we											
